

Prepared by: Richard Drapeau
 Project: RW Creteau Technology Center
 General Contractor: Harvey Construction

Date: Thu 7/19/18

Weather Conditions

Sunny / 80-55

Onsite Construction Personnel

<i>Subcontractor</i>	<i>Approx. Number of Personnel</i>	<i>Comments</i>
Harvey Construction:	1-Superintendent 1-Labor	Supervising Phase-1 demolition and gas line extension.
Carter Sprinkler	0-Labor	Not on site
Interstate Elec.	1-Foreman 2-Labor	Continuing Phase-1 classroom demo and electrical make safe. Rough-in new classroom wiring
Johnson & Jordon	1-Foreman 5-Journeymen 6-Duct Clean	Continued demo of existing ductwork. Continued duct cleaning (Armstrong)
NH Demolition	1-Foreman 5-Labor	Continuing Phase-1 classroom demo Rm. 120 corner office
Red Star Building Systems	0-Labor	Not on site
SD Szetela Masonry	1-Forman 5-Labor	Setting up for shear wall block extension at Rms.210-220
SW Cole	0-Tech	Not on site
Unitil / NEUCO	1-Foreman 5-Labor	Installed 2" gas line at west side of building. Asphalt patching at new gas line trenches.

Photos:

Rm. 200 Shear Wall Block & Trusses 7-19-18




Rm. 210 Duct Cleaning Phase-1 2nd Fl. 7-19-18



Rm. 210-220 Staged Shear Wall Block 7-19-18 (1)



Rm. 228-232 New Wall Elec. Rough-In 7-19-18

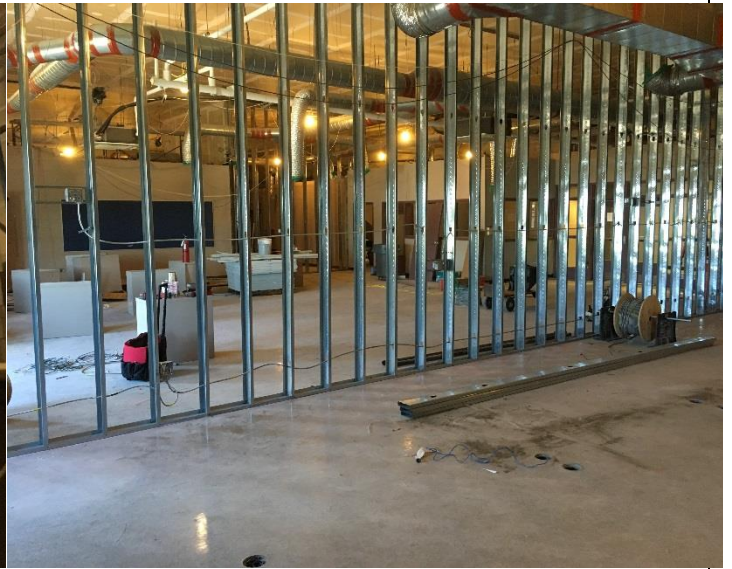

Rm.120 Corner Office Demo 7-19-18

**Unitil 2" Gas Line @ West Side & Asphalt
Patching At All Trench Locations 7-19-18**

