

Prepared by: Richard Drapeau  
 Project: RW Creteau Technology Center  
 General Contractor: Harvey Construction

Date: Wed 7/18/18

**Weather Conditions**


Sunny / 82-54

**Onsite Construction Personnel**

<i>Subcontractor</i>	<i>Approx. Number of Personnel</i>	<i>Comments</i>
Harvey Construction:	1-Superintendent 0-Labor	Supervising Phase-1 demolition and gas line extension.
Carter Sprinkler	0-Labor	Not on site
Interstate Elec.	1-Foreman 4-Labor	Continuing Phase-1 classroom demo and electrical make safe. Rough-in new classroom wiring
Johnson & Jordon	6-Labor	Continued demo of existing ductwork. Conducting duct cleaning (Armstrong)
NH Demolition	1-Foreman 5-Labor	Continuing Phase-1 classroom demo
Red Star Building Systems	0-Labor	Not on site
SD Szetela Masonry	1-Forman 6-Labor	Continued shear wall block at Rm.210.
SW Cole	0-Tech	Not on site
Unittel / NEUCO	1-Foreman 5-Labor	Cut & cap existing gas line at east side of building

**Photos:**

**Corridor 209 Sample Flooring 7-18-18**

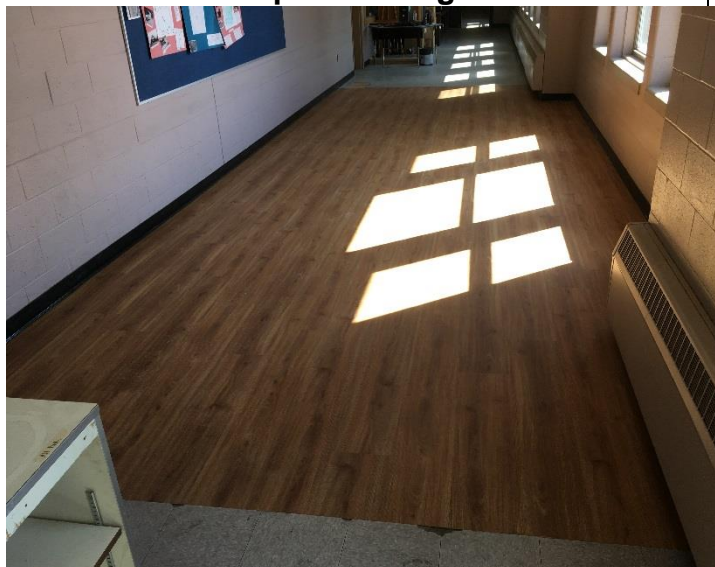

**Duct Cleaning Phase-1 2nd Fl. 7-18-18 (2)**



**Rm. 200 Shear Wall Block 7-18-18 (1)**



**Rm. 200 Shear Wall Block 7-18-18 (2)**



**Rm. 210 Shear Wall Staged Block 7-18-18**



**Unitil Cut & Cap Existing Line @ E Side Of Bldg. 7-18-18**

