

Prepared by: Richard Drapeau  
Project: R.W. Creteau Technology Center  
General Contractor: Harvey Construction

Date: Tue 7/24/18

**Weather Conditions**


Cloudy-PM Showers / 80-68

**Onsite Construction Personnel**

<i>Subcontractor</i>	<i>Approx. Number of Personnel</i>	<i>Comments</i>
Harvey Construction:	1-Superintendent 1-Labor	Supervising Phase-1 demolition and renovation 2 PM OAC Meeting
Carter Sprinkler	0-Labor	Not on site
Interstate Elec.	1-Foreman 4-Labor	Continuing Phase-1 classroom demo and electrical make safe. Rough-in new classroom wiring
Johnson & Jordon	1-Foreman 5-Journeymen 6-Duct Clean	Continued demo of existing mechanical piping & ductwork.
NH Demolition	1-Foreman 5-Labor	Continuing Phase-1 classroom demo
Red Star Building Systems	2-Labor	1 <sup>st</sup> & 2 <sup>nd</sup> Fl. classroom framing.
SD Szetela Masonry	1-Forman 5-Labor	shear wall CMU grouting.
SW Cole	1-Tech	Test & inspect CMU grout placement

**Photos:**

**1st Fl. Elec. Demo 7-24-18**

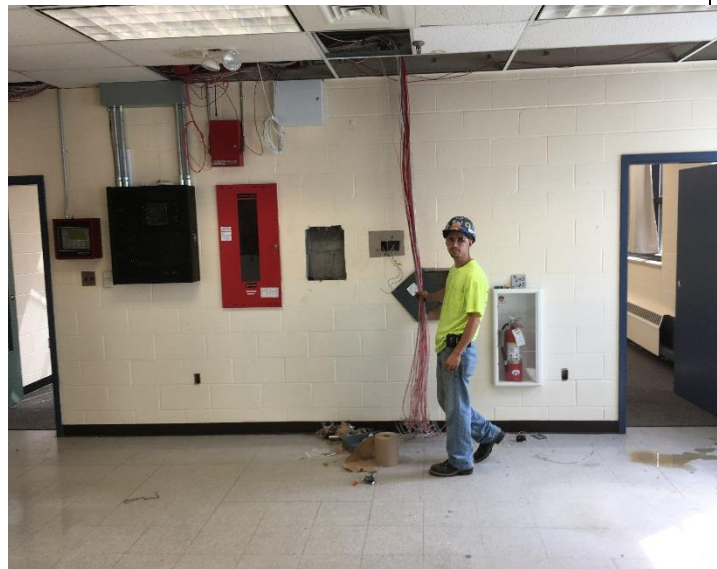

**Rm.230 Flooring Demo 7-24-18**



2nd Fl. Mech. Rm. Duct Demo 7-24-18 (1)



2nd Fl. Mech. Rm. Duct Demo 7-24-18 (2)



Rm.210 CMU Grout Placement 7-24-18 (1)



Rm.210 CMU Grout Placement 7-24-18 (2)

