

Prepared by: Richard Drapeau
Project: R.W. Creteau Technology Center
General Contractor: Harvey Construction

Date: Wed 7/25/18


Weather Conditions

Cloudy-PM Showers / 80-68

Onsite Construction Personnel

<i>Subcontractor</i>	<i>Approx. Number of Personnel</i>	<i>Comments</i>
Harvey Construction:	1-Superintendent 1-Labor	Supervising Phase-1 demolition and renovation 9AM-Wall framing inspection 11AM-New wall electrical rough-in inspection
Carter Sprinkler	2-Labor	Begin new sprinkler piping
Interstate Elec.	1-Foreman 4-Labor	Phase-2 electrical / data rough-in
Johnson & Jordon	1-Foreman 5-Journeymen	Installing Phase-2 gas piping
NH Demolition	1-Foreman 5-Labor	Continuing Phase-1 classroom demo. Rm.230 VCT and Rm. 201 CMU for new door location
Red Star Building Systems	0-Labor	Not on site
SD Szetela Masonry	1-Forman 5-Labor	Corridor shear wall CMU grouting and Rm. 220 shear wall block
SW Cole	0-Tech	Not on site

Photos:

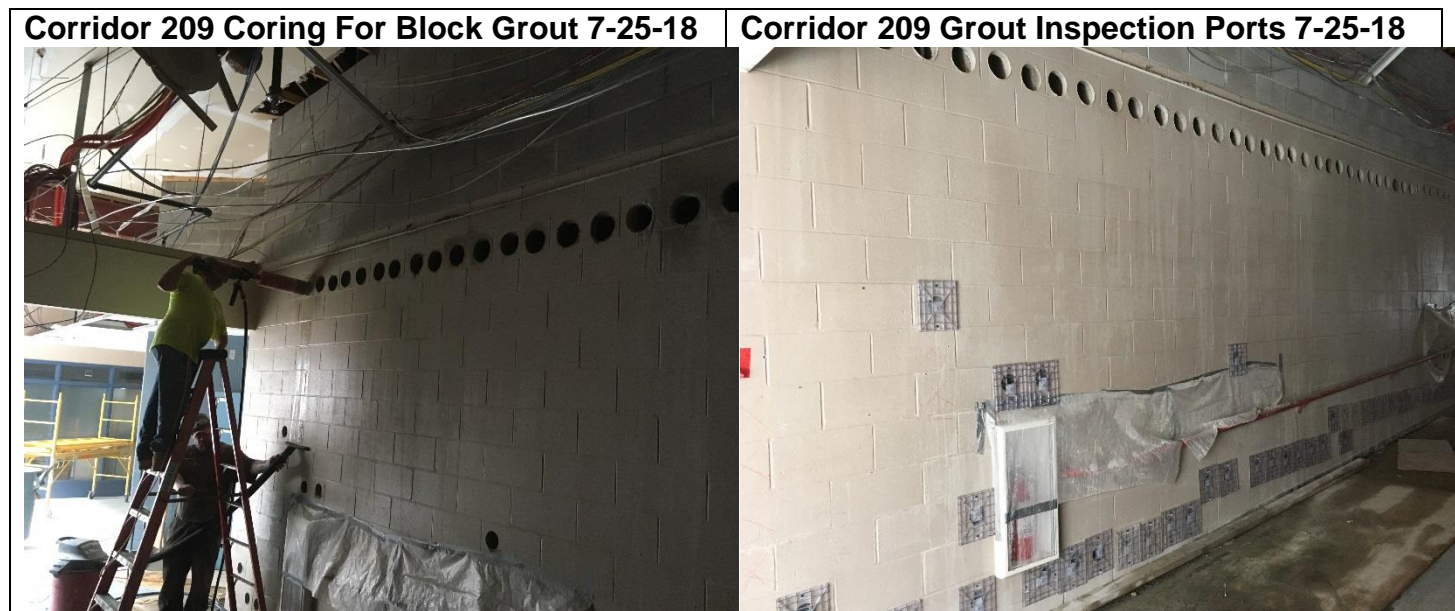

Main Lobby Temp Construction Wall 7-25-18



Rm.228 Shear Wall Block 7-24-18



Rm.230 Block Demo For New Door 7-24-18



Rm.232 Flooring Demo 7-24-18

